

REPORT ON BOILERS.

No. 6450

19 APR 1945

Received at London Office.

Date of writing Report **8th Feb. 1945** When handed in at Local Office **8th Feb. 1945** Port of **Vancouver, B.C.**

No. in Survey held at **Vancouver, B. C.** Date, First Survey **23rd Nov. 1944** Last Survey **31st Jan. 1945**

on the **Steel Single Screw Steamer "FAIRMOUNT PARK"** (Number of Visits **34**)

Built at **Vancouver, B.C.** By whom built **Burrard Dry Dock Co.** Yard No. **227** When built **1945** Tons {Gross **7145.02** Net **4209.66**

Engines made at **Lachine, P.Q.** By whom made **Canadian Allis Chalmers Ltd.** Engine No. **388** When made **1945**

Boilers made at **Vancouver, B.C.** By whom made **Dominion Bridge Co. Ltd.** Boiler No. **788, 789, 791** When made **1945**

Nominal Horse Power **505** Owners **Minister of Munitions & Supply of Canada. (Mgrs. Park Steamship Co. Ltd.)** Port belonging to **Montreal, P.Q.**

MULTITUBULAR BOILERS—MAIN, AUXILIARY, OR DONKEY:

Manufacturers of Steel **Worth Steel Co., American Welding Co., Lukins Steel Co., Bethlehem Steel Co.** (Letter for Record **S**)

Total Heating Surface of Boilers **7140 sq. ft. total** Is forced draught fitted **Yes** Coal or Oil fired **Either**

No. and Description of Boilers **Three - Single Ended Cylindrical Multitubular** Working Pressure **220 lbs. per square inch**

Tested by hydraulic pressure to **380 lbs.** Date of test **29-11-44, 4-12-44, 7-12-44** No. of Certificate **788, 789, 791** Can each boiler be worked separately **Yes**

Area of Firegrate in each Boiler **51 sq. ft.** No. and Description of safety valves to each boiler **Two - 2-1/4" Morrison High Lift**

Area of each set of valves per boiler {per Rule **6.35 sq. ins.** as fitted **7.95 sq. ins.** Pressure to which they are adjusted **220 lbs.** Are they fitted with easing gear **Yes**

In case of donkey boilers, state whether steam from main boilers can enter the donkey boiler **No Donkey Boiler**

Smallest distance between boilers or uptakes and bunkers or woodwork **2 ft.** Is oil fuel carried in the double bottom under boilers **No**

Smallest distance between shell of boiler and tank top plating **2 ft.** Is the bottom of the boiler insulated **Yes**

Largest internal dia. of boilers **14'-6-3/16"** Length **11'9" Ext.** Shell plates: Material **O.H. Steel** Tensile strength **65000-77000 lbs.**

Thickness **1-13/32"** Are the shell plates welded or flanged **No** Description of riveting: circ. seams {end **Double** inter **---** long. seams **1-1/2"** Pitch of rivets {plate **---** rivets **---**

Percentage of strength of circ. end seams {plate **64.2%** rivets **47.6%** Percentage of strength of circ. intermediate seam {plate **---** rivets **---**

Percentage of strength of longitudinal joint {plate **85.1%** rivets **92.8%** combined **88.7%** Working pressure of shell by Rules **221.2 lbs.**

Thickness of butt straps {outer **1-3/32"** inner **1-7/32"** No. and Description of Furnaces in each Boiler **3 Morrison Corrugated Stephen Gourlay**

Material **O.H. Steel** Tensile strength **55000 - 65000 lbs.** Smallest outside diameter **41-9/16"** end

Length of plain part {top **10"** bottom **10"** Thickness of plates {crown **21/32"** bottom **---** Description of longitudinal joint **Forge Weld**

Dimensions of stiffening rings on furnace or c.c. bottom **---** Working pressure of furnace by Rules **230.9 lbs.**

End plates in steam space: Material **O.H. Steel** Tensile strength **55000-65000 lbs.** Thickness **1-15/32"** Pitch of stays **21" x 21"**

How are stays secured **Double Nuts & 6-3/4" x 1/4" washer each end** Working pressure by Rules **230.3 lbs.**

Tube plates: Material {front **O.H. Steel** back **O.H. Steel** Tensile strength {55000-65000 lbs. 58000-68000 lbs. Thickness {1" 13/16"

Mean pitch of stay tubes in nests **9.8"** Pitch across wide water spaces **8-1/4" x 14-1/2"** Working Pressure {front **245 lbs.** back **247 lbs.**

Orders to combustion chamber tops: Material **O.H. Steel** Tensile strength **65000 - 75000 lbs.** Depth and thickness of girder

Centre **10-1/4" x 7/8"** Length as per Rule **34"** Distance apart **11"** No. and pitch of stays

each **3 - 7-3/8"** Working pressure by Rules **261.6 lbs.** Combustion chamber plates: Material **O.H. Steel**

Tensile strength **58000 - 68000 lbs.** Thickness: Sides **25/32"** Back **23/32"** Top **25/32"** Bottom **25/32"**

Pitch of stays to ditto: Sides **9" x 10-3/16"** Back **9" x 8 1/2"** Cent. C.C. **7-3/8" x 11"** Are stays fitted with nuts or riveted over **Nuts**

Working pressure by Rules **224 lbs.** Front plate at bottom: Material **O.H. Steel** Tensile strength **55000-65000 lbs.**

Thickness **1"** Lower back plate: Material **O.H. Steel** Tensile strength **55000-65000 lbs.** Thickness **15/16"**


Pitch of stays at wide water space **9" x 14-1/2"** Are stays fitted with nuts or riveted over **Nuts**

Working pressure **232 lbs.** Main stays: Material **O.H. Steel** Tensile strength **63000-73000 lbs.**

Diameter {At body of stay **3-1/2"** Over threads **3-3/4"** No. of threads per inch **6** Area supported by each stay **441 sq. ins.**

Working pressure by Rules **245 lbs.** Screw stays: Material **O.H. Steel** Tensile strength **58000-68000 lbs.**

Diameter {At turned off part, **1.606** Over threads **1.75"** No. of threads per inch **9** Area supported by each stay **81 sq. ins.**

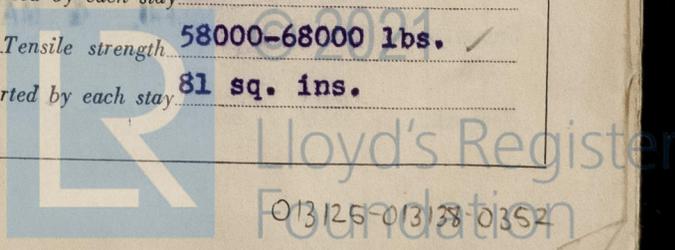

Working pressure by Rules **224 lbs.** Are the stays drilled at the outer ends **No** Margin stays: Diameter { At turned off part, **1.856"** or Over threads **2"**

No. of threads per inch **9** Area supported by each stay **105.75 sq. in.** Working pressure by Rules **232 lbs.**

Tubes: Material **O.H. Steel** External diameter { Plain **3"** Stay **3"** Thickness { **.16"** **3/8"** No. of threads per inch **9**

Pitch of tubes **4-1/8" x 4-1/4"** Working pressure by Rules **250 lbs.** Manhole compensation: Size of opening

End plate **16" x 12"** Section of compensating ring **--** No. of rivets and diameter of rivet holes { Upper **4-1/4"** Lower **3-1/2"** Steam Dome: Material **--**

Outer row rivet pitch at ends **--** Depth of flange if manhole flanged **--** Tensile strength **--** Thickness of shell **--** Description of longitudinal joint **--**

Diameter of rivet holes **--** Pitch of rivets **--** Percentage of strength of joint { Plate **--** Rivets **--**

Internal diameter **--** Working pressure by Rules **--** Thickness of crown **--** No. and diameter stays **--** Inner radius of crown **--** Working pressure by Rules **--**

How connected to shell **--** Size of doubling plate under dome **--** Diameter of rivet holes and pitch of rivets in outer row in dome connection to shell **--**

Type of Superheater **"ELESCO" Smoke Box Type** Manufacturers of { Tubes **(National Tube Co. Ellwood City, Pa.)** Steel forgings **(Pa.)** Steel castings **(Pa.)** Internal diameter and thickness of tubes **.69" .095" (B.B.W. Min.)**

Number of elements **58** Material of tubes **S.D. Steel** Tensile strength **35.5 Tons** Thickness **1-1/8" Min.** Can the superheater be shut off the boiler be worked separately **No** Is a safety valve fitted **Yes**

Area of each safety valve **1.767 sq. ins.** Are the safety valves fitted with easing gear **No** Working pressure as Rules **520 lbs. per sq. in.** Pressure to which the safety valves are adjusted **220 lbs. per sq. in.** Hydraulic test pressure tubes **2500 lbs. per sq. in.** forgings and castings **550 lbs. per sq. in.** and after assembly in place **Steam Test** Are drain cocks valves fitted to free the superheater from water where necessary **Yes**

Have all the requirements of Sections 14 to 22 inclusive for boilers been complied with **Yes**

The foregoing is a correct description.
Dominion Bridge Co. Limited
J. J. Gross Manufacturer

Dates of Survey { During progress of work in shops - - } **1944. Nov. 23, 24, 27, 28, 29. Dec. 4, 7, 8.** Are the approved plans of boiler and superheater forwarded herewith **Yes** (if not state date of approval.)

{ During erection on board vessel - - } **1944. Dec. 19, 22, 23, 27, 28, 29, 30. 1945. Jan. 2, 3, 4, 5, 6, 8, 9, 10, 11, 12, 13, 17, 18, 20, 23, 25, 27, 29, 31.** Total No. of visits **34**

Is this Boiler a duplicate of a previous case **Yes** If so, state Vessel's name and Report No. **S.S. "WINONA PARK" Ver. Rpt. No. 642**

GENERAL REMARKS (State quality of workmanship, opinions as to class, &c.)

These boilers have been constructed under Special Survey of tested materials in accordance with the approved plans, New York letters and otherwise in conformity with the Society's Rules. On completion the boilers were satisfactorily tested under hydraulic pressure to 380 lbs. per sq. inch. They were fitted on board under Special Survey, examined under working conditions, safety valves adjusted under steam to the working pressure and a satisfactory accumulation test carried out.

Cross seams of both end plates are fusion welded by Union Melt Process; stress relieved under Survey. Welds ground flush both sides of plate. Combustion chamber wrapper plates welded to back tube plate and combustion chamber back plate; butts of combustion chamber wrapper plates also welded, all hand welding, tested as per Rule and ground flush.

Survey Fee **\$150.00** When applied for **1st Feb. 1945** *RB*

Travelling Expenses (if any) **15.00** When received **19**

Retired For Mr. W.E. Baillie & Co. *R.B.M. Solem*
 Engineer Surveyor to Lloyd's Register of Shipping

Committee's Minute **FRI. 4 MAY 1945**

Assigned **Su F.E. machy rph**



© 2021

Lloyd's Register Foundation
