

Defender
24.5

EXT
LIV
16/9/32

Index No. **29460**
(For London Office only.)
THU. FEB 17 1921
No. **40876**

Lloyd's Register of Shipping.

SURVEYS FOR FREEBOARD.—STEAM SHIPS.

PARTICULARS RELATING TO ALL STEAM SHIPS EITHER FLUSH DECKED, OR WITH TOP GALLANT FORECASTLES, SHORT POOPS AND BRIDGE HOUSES DISCONNECTED, OR WITH TOP GALLANT FORECASTLES HAVING LONG POOPS, OR RAISED QUARTER DECKS CONNECTED WITH BRIDGE HOUSES, OR OTHERWISE.

Port of Survey **Glasgow**
Date of Survey **While building**
Name of Surveyor **Henry Hibbs**

Messrs G Bounell & Co. N° 382.

Ship's Name	Port of Registry and Nationality	Official Number	Gross Tonnage	Date of Build.	Particulars of Classification.
"DIPLOMAT"	Liverpool British	145878	8260	1921	100 A1 (contemplated)

Registered Dimensions from Register.	LENGTH.	BREADTH.	DEPTH.	UNDER DECK TONNAGE.
	482.15	58.4	33.45	7156.87
Length on ADLINE.	480.16	Mean Frame Depth 11 1/2 Rule 76 1/2 44 1/2 71 1/2 80	Ceiling fitted 1.11 Sheer 1.11 Tank rises 2 at margin -25 tons	Peak Framing Tank in tween decks say -25 tons
CORRECTED DIMENSIONS.	480.16	57.69	34.56	7131.87

Efficient of fineness..... **.74** ✓ **.745**
Any modification necessary } **Tank rises at Margin**
[Para. 4 (a) to (e)]*
Efficient as corrected **.74** ✓

Mean Stem..... **134**
Sternpost ... **62**
 $196 \div 2 = 98$... Mean **98**
Mean at 1/3 of the length from Stem **73.75**
Sternpost **34.125**
 $107.875 \div 2 = 53.9375$ Mean **53.94**
Actual mean Sheer **98**
Standard mean Sheer [Table, Para. 18] **58**
Difference..... **40** $\div 4 = -10$
If limited as Para. 18 (f) ✓

Rise in Sheer }
amidships }
Para. 18 (e) }
At front of bridge house.....
At after end of forecastle ✓
Fall in Sheer }
Para. 18 (d) }
Length uncovered ✓
Correction

ALLOWANCE FOR DECK ERECTIONS :—
Freeboard, Table C..... **(9'-9 1/2") - (3'-2")** **6'-7 1/2"**
Correction for Length, if required (Para. 12, 13, and 14) ✓
Freeboard by Table A, corrected for sheer, and for length, if required (Para. 12, 13, and 14) }
Difference **8'-11 1/2"**
Percentage **2.4**
Percentage as below..... **40%**
Correction for R. Q. Dk. if engine and boiler openings not covered by bridge house (Para. 11) }
Allowance for Deck Erections **-11 1/2"**

	Length.	Length allowed.	Height.
Forecastle.....	51.16	51.16	7.5
Bridge House.....	187.5	183.56	8.0
Quarter Deck.....	54.29	54.04	7.25
Poop.....	54.29	54.04	7.25
Total.....	288.76	288.76	
Length of Ship.....	480.16	480.16	.60
Corresponding percentage (Para. 11, 12, 13, or 14) } 40% ✓ 289.01 $\div 480.16 = .60$			

FREEBOARD recommended amidships from centre of Disc to top of Statutory Deck Line, Wood (Iron) Deck :—	
Fresh Water Line	above centre of Disc
Indian Summer Line	" " "
Winter Line	below " " "
Winter North Atlantic Line	" " "

Moulded Depth as measured..... **35'-10"**
Addition for Keel below base line for draught record..... **3 1/2** inches.

CORRECTION FOR LENGTH.
Length of Ship on Loadline..... **480.16** ✓
Length in Table **430.0** ✓
Difference **50.16** ✓
Correction for 10ft., Table A. **1.7** ✓ Table C.
× Difference divided by 10 **8.52** (if required.)
If 1/10ths length covered divide by 2 **+ 4 1/2** ✓

CORRECTION FOR IRON DECK.
Proportion covered, if less than 1/10ths length covered **.60** ✓
Thickness of usual wood deck, less stringer **3 1/2"** **- 2"** ✓

CORRECTION FOR ROUND OF BEAM.
Breadth at Gunwale amidships..... **58.0** ✓
Round of Beam **17"** ✓
Normal round..... **14 1/2** ✓
Difference **2 1/2** $\div 2 =$ **1 1/4** ✓
Proportion of Deck uncovered (Para. 19) **1** **- 1/2** ✓

Freeboard, Table A **9'-9 1/2"**
Correction for Sheer **- 10** ✓
Correction for Length **+ 4 1/2** ✓
Allowance for Deck Erections **- 11 1/2** ✓
Correction for Round of Beam..... **- 1 1/4** ✓
Correction for fall in Sheer (if any)..... **- 2** ✓
Correction for Iron Deck (if required) ✓
Additions for non-compliance with provisions of }
Para. 11 (d) and (e) } ✓
Other Corrections (if any) ✓

Winter Freeboard **8'-1 3/4"**
Summer Freeboard **7'-7 1/4"**
Indian Summer Freeboard **7'-0 1/4"**
N.A. Winter Freeboard ✓
Correction necessary because clearside amidships, measured in accordance with the Statute is not taken at the intersection of the wood or iron deck with side. }
..... **02** ✓

Winter Freeboard from deck line **8'-3 3/4"**
Summer " " " **7'-9 1/4"**
Indian Summer " " " **7'-2 1/4"**
N.A. Winter " " " ✓
Winter Freeboard from deck line **7'-9** ✓
Summer " " " **7** ✓
Indian Summer " " " **7 1/2** ✓
N.A. Winter " " " ✓

If the frames, skin planking, or ceiling are of unusual thickness the breadth of vessel to inside of ceiling should be reported if possible.
In vessels obtaining an allowance for deck erections under Para. 11 where the sheer drops abaft amidships the height of the R.Q.D. is to be taken from the level of the top of the amidship beam.
In flush-decked vessels the total standard mean sheer means the sheer measured at the stem and sternpost. In vessels having poops and forecastles, it means the sheer measured at points distant one-eighth of the vessel's length from stem and sternpost.

State dimensions of freeing port area on back of this form.
The Surveyor should state whether the fall in sheer as reported is measured relatively to the straight line of keel or to the water line. If measured relatively to water line the vessel's draft at time of survey, and also the usual load draft forward and aft should be reported.

W 382-0047

© 2021
Lloyd's Register
MARINE REPORT
REGISTERED 29-3-21
Foundation

Do all the Frames extend to the top height in the Poop? *Yes* Raised Quarter Deck? ☒ Bridge House? *Yes* Forecastle? *Yes*
 To what height do the Reverse Frames extend? *Main Dh.*
 Has the Poop or Raised Quarter Deck an efficient Iron Bulkhead at the fore end? *Yes*
 Give particulars of the means for closing the openings in Bulkhead *Wood doors*
 Is the Poop or Raised Quarter Deck connected with the Bridge House? *No* Has the Bridge House an efficient Bulkhead at the fore end? *Yes*
 Give particulars of the means for closing the openings in Bulkhead *No openings*
 What is the thickness of the Bridge Front plating? *1/2"* and Coaming plate? *1/2"*
 Give scantlings and spacing of the Stiffeners *9 x 3 x .64 Bulb angles spaced 30"*
 Are bracket plates fitted at each end of the Stiffeners? *Yes* Are hor'l. brackets fitted connecting Bridge Bulk'd. with Bulwarks? *Yes*
 Has the Bridge House an efficient Iron Bulkhead at the after end? *Yes*
 How are the openings closed? *Storm boards half height 9'-9" forward of aft end of bridge in riveted channels*
 Is the Forecastle at least as high as the main or top-gallant rail? *Yes* Has the Forecastle an efficient Iron or Wood Bulk'd. at after end? *Open*
 Are the Engine and Boiler openings covered by a Bridge, Poop, Raised Quarter Deck, or enclosed by a Strong Iron or Steel Deckhouse? *Yes*
 If the openings are not so protected are the exposed parts of the Casings efficiently constructed? ☒
 Give thickness of plating; scantlings and spacing of Stiffeners. ☒
 What is the height of the exposed Casings? ☒ Are suitable means provided for closing all openings in them in bad weather? ☒

Are the Weather Deck Hatchways efficiently constructed and at least equal to the requirements of Section 20 of the Rules for 1904-5? Give particulars below: *Yes*

Position and Size.	N ^o 1		N ^o 2		N ^o 3		N ^o 4		N ^o 5		N ^o 6		N ^o 7	
Item.	Ship.	Rule.	Ship.	Rule.	Ship.	Rule.	Ship.	Rule.	Ship.	Rule.	Ship.	Rule.	Ship.	Rule.
Height above top of DECK	30"	30"	30"	30"	30"	30"	30"	30"	30"	30"	30"	30"	30"	30"
COAMING Thickness	Sides 10/16	10/16	10/16	10/16	10/16	10/16	10/16	10/16	10/16	10/16	10/16	10/16	10/16	10/16
Ends	"	"	"	"	"	"	"	"	"	"	"	"	"	"
SHIFTING BEAMS OR WEB PLATES	Number 2	6	3	2	2	5	3							
Section and Scantlings	16 x .35	14 x .34	13 x .36	15 x .35	13 x .33	14 x .34	15 x .35							
Material	steel	steel	steel	steel	steel	steel	steel							
* FORE AND AFTERS	Number													
Section and Scantlings	No fore & afters													
Material														
HATCHES Thickness	3"	3"	3"	3"	3"	3"	3"	3"						
Remarks	7 x 3 x .40 on sides, brackets at ends as per plan.													

* The depth of Fore and Afters should be stated from the underside of the hatches in all cases.

(If the sill of the lowest side scuttle will be less than 6 inches above the Indian Summer Load Line if assigned under the tables, state vertical distance from top of deck at side amidships to lower edge of lowest side scuttle.)

The following information is to be given in all Cases of vessels dealt with under Paras. 11, 12 (under 15 feet Moulded depth) and under Shelter Deck Rules.

What is the thickness of the Bridge Sheerstrake? _____ Strake between Main and Bridge Sheerstrakes? _____

Delete the words { The Crew are, are not, berthed in the bridge house.

that do not apply { The arrangements to enable them to get backwards and forwards from their quarters are, are not satisfactory.

Length of Bulwarks in well _____

Area of Freeing Ports required by Para. 11 (e) each side of vessel = _____ Sq. ft.


Ft. Tenths. Ft. Tenths. No.

1 x 10 1 x 10

Freeing Ports (each side of vessel)

= _____ Sq. ft.

Total deficiency or excess = _____ Sq. ft.

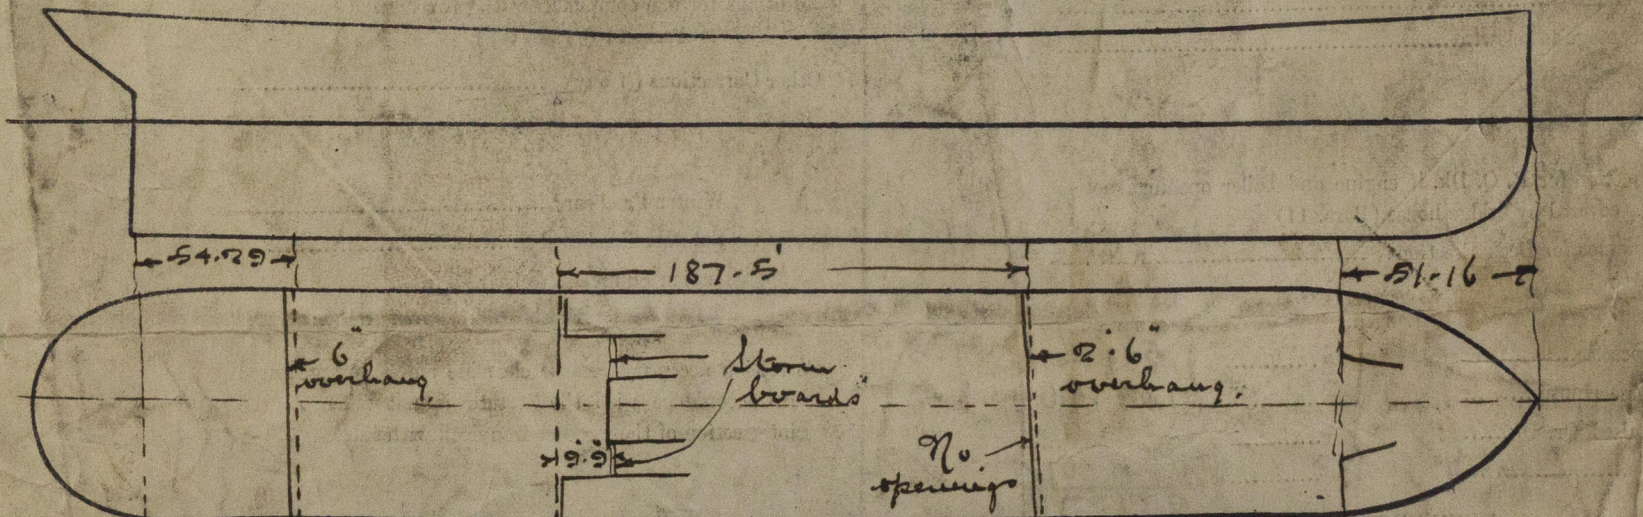

Show hereon line of Floors or Tank Top with position of any Breaks in same; also height of Peak Tank tops, &c., &c.

State any special features in the construction of the Vessel *Vessel to be classed 100 A1.*
Midships section. Profile & freeboard request enclosed.
Sister vessel to S/S "Defender" L.R. report N^o 35061
 Owners *T & J Harrison.*

" Address _____

Fee £ 13 : 0 : 0 Received by me _____



16/2/21 *HL*

Lloyd's Register Foundation
